


SILT FENCE DETAIL SILT SACK DETAIL

- SOIL EROSION CONTROL NOTES:
1. ALL SOIL EROSION CONTROL MEASURES ARE TO BE IN PLACE PRIOR TO THE START OF ANY GRADING.
 2. INSPECT & MAINTAIN ALL TEMPORARY SOIL EROSION CONTROLS AFTER EACH SIGNIFICANT RAINFALL EVENT UNTIL THE SITE HAS BEEN PERMANENTLY STABILIZED
 3. ALL NON PAVED AREAS TO BE TOPSOILED (6" MINIMUM) & SEEDED.
 4. PROTECT 9 NEW STORM INLETS WITH SILT SACKS PER DETAIL & REMOVE WHEN SITE IS STABILIZED.
 5. ALL DISTURBED BANKS EQUAL TO OR GREATER THAN 3:1 BE COVERED WITH TOPSOIL, SEED & NORTH AMERICAN GREEN S-150 (OR APPROVED EQUAL) EROSION CONTROL BLANKET. THIS BLANKET, ALONG WITH THE NECESSARY STAPLES OR WOOD PEGS, SHALL BE PLACED PER MANUFACTURER'S RECOMMENDATIONS. SEAMS SHALL BE PLACED PARALLEL TO THE DIRECTION OF SURFACE RUNOFF.
 6. PLACE SILT FENCE AS SHOWN ON PLAN & PER DETAIL.
 7. PLACE SILT SACKS AS SHOWN ON PLAN & PER DETAIL.


SCALE : 1"=30'
1' CONTOUR INTERVAL

LEGEND

- = IRON STAKE FOUND
- = IRON STAKE SET
- = MONUMENT
- ☐ = TELEPHONE BOX
- ⊕ = HYDRANT
- ⊖ = VALVE
- ⊞ = CATCH BASIN
- = MANHOLE
- ⊞ = BURIED WATERMAIN MARKER
- 614 — = EXISTING CONTOUR
- - - 614 - - - = PROPOSED CONTOUR
- 614.00 = PROPOSED SPOT ELEVATION



Know what's below.
Call before you dig.

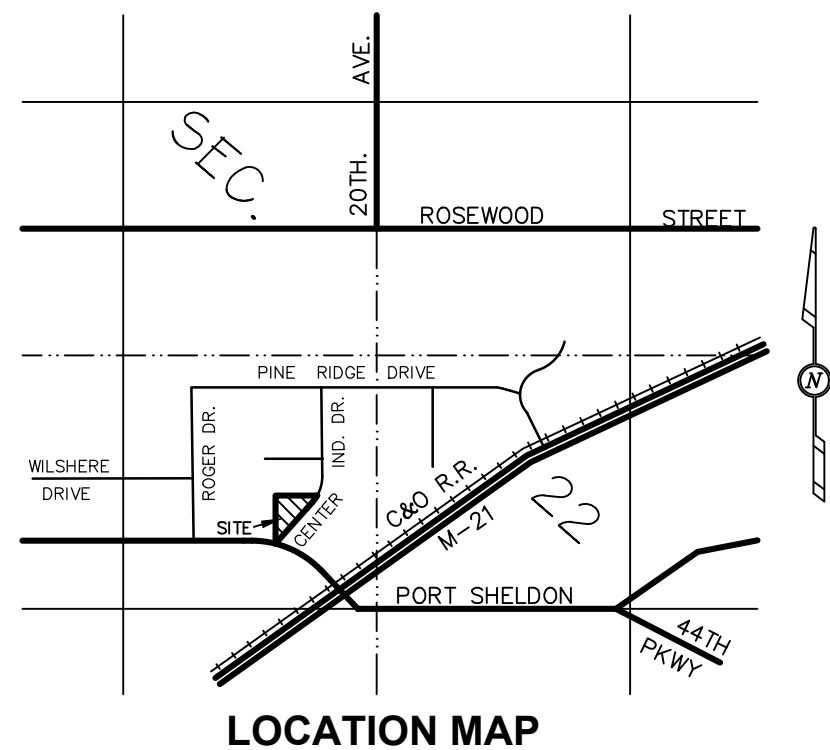

GRADING + SOIL EROSION CONTROL PLAN
6555 CENTER INDUSTRIAL DRIVE

FOR: TODD PONSTEIN
6601 WILSHIRE
JENISON, MI 49428

IN: PART OF THE SW 1/4 OF SECTION 22, T6N, R13W,
GEORGETOWN TOWNSHIP, OTTAWA COUNTY, MICHIGAN.

REVISIONS:	



DRAWN BY: MK	PROJ. ENG.: DJS	SHEET 2 of 2
APPROVED BY: DJS	PROJ. SURV.: .	
FILE NO.: 972762E	DATE: 07-28-16	

08-31-16 REV PER ZONING ADMINISTRATOR (mk)
